

WHITE HALL DAM - COMPLETED


DATA

Watershed: Gunpowder
Stream: Little Falls, Tributary to Big Falls
Stream Order: 4th Order
County: Baltimore County
Location: Weisburg Ave, Near White Hall MD
Lat/Long: N39*37.290' W076*37.817'
Cong. District: MD 06
Ownership: Private
Point of Contact: Jim Thompson - DNR
Structure Type: Concrete Dam
Type of Passage: Removal/Bypass
Miles Reopened: 16 miles.
Target Species: Brown Trout, Rainbow Trout
Start / Finish Date: Fall/Winter 2010

PROJECT BUDGET

Project Partner	Design	Construction
Estimated Cost	\$85K	\$221,866
FAF/CBT		\$30,500
NRCS	\$87,396	\$159,077
DNR Fisheries		\$35,000
FWS		\$7,391/\$1,800
Total	\$87,396	\$198,768

Codes: (S)-Secured, (A)-Applied

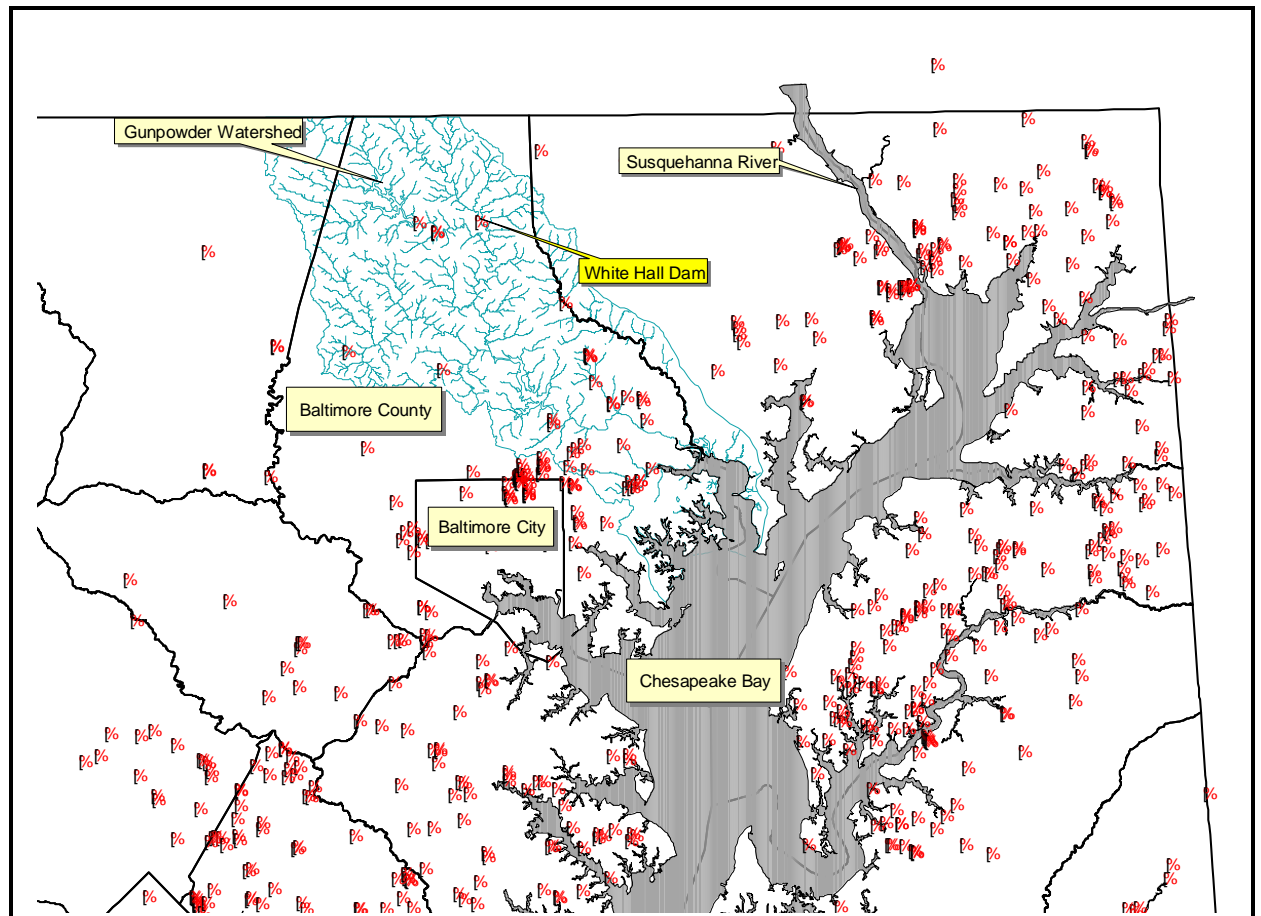

COMMENTS

LAST UPDATED – 12/05/2011

The Whitehall Dam was removed in August of 2011 providing passage to wild reproducing brown trout and alleviating thermal pollution impacts. Hurricane Irene and Tropical Storm Lee caused significant damage to the project site in late August. Fortunately the National Resources Conservation Service (NRCS) secured last-minute funding to repair the structures and regrade the banks.

PROJECT PICTURES



BEFORE



AFTER
