

PROFESSIONAL CERTIFICATION

I HEREBY CERTIFY THAT THESE DOCUMENTS WERE PREPARED OR APPROVED BY ME, AND THAT I AM A DULY LICENSED PROFESSIONAL ENGINEER UNDER THE LAWS OF THE STATE OF MARYLAND.

NAME: WILLIAM WU
LICENSE NO. 53359
EXPIRATION DATE: 2024-10-22



APPLETON ROAD BRIDGE REPLACEMENT

AT
FAIR HILL N.R.M.A.
CECIL COUNTY, MD
USING AGENCY APPROVAL

NAME _____ DATE _____

TITLE _____

DEPARTMENT OF GENERAL SERVICES APPROVAL

PROJECT MANAGER _____ DATE _____

CHIEF PROJECT MGT. & DESIGN _____ DATE _____

MARK _____ DATE _____ DOCUMENTS _____

CAD DWG FILE: RK&K

DRAWN BY: MBP

CHECKED BY: CMS/MT


PROJECT NO.: P-001-190-110

DATE: AUGUST, 2023

DETOUR PLAN

MOT.2

SHEET 5 OF 27

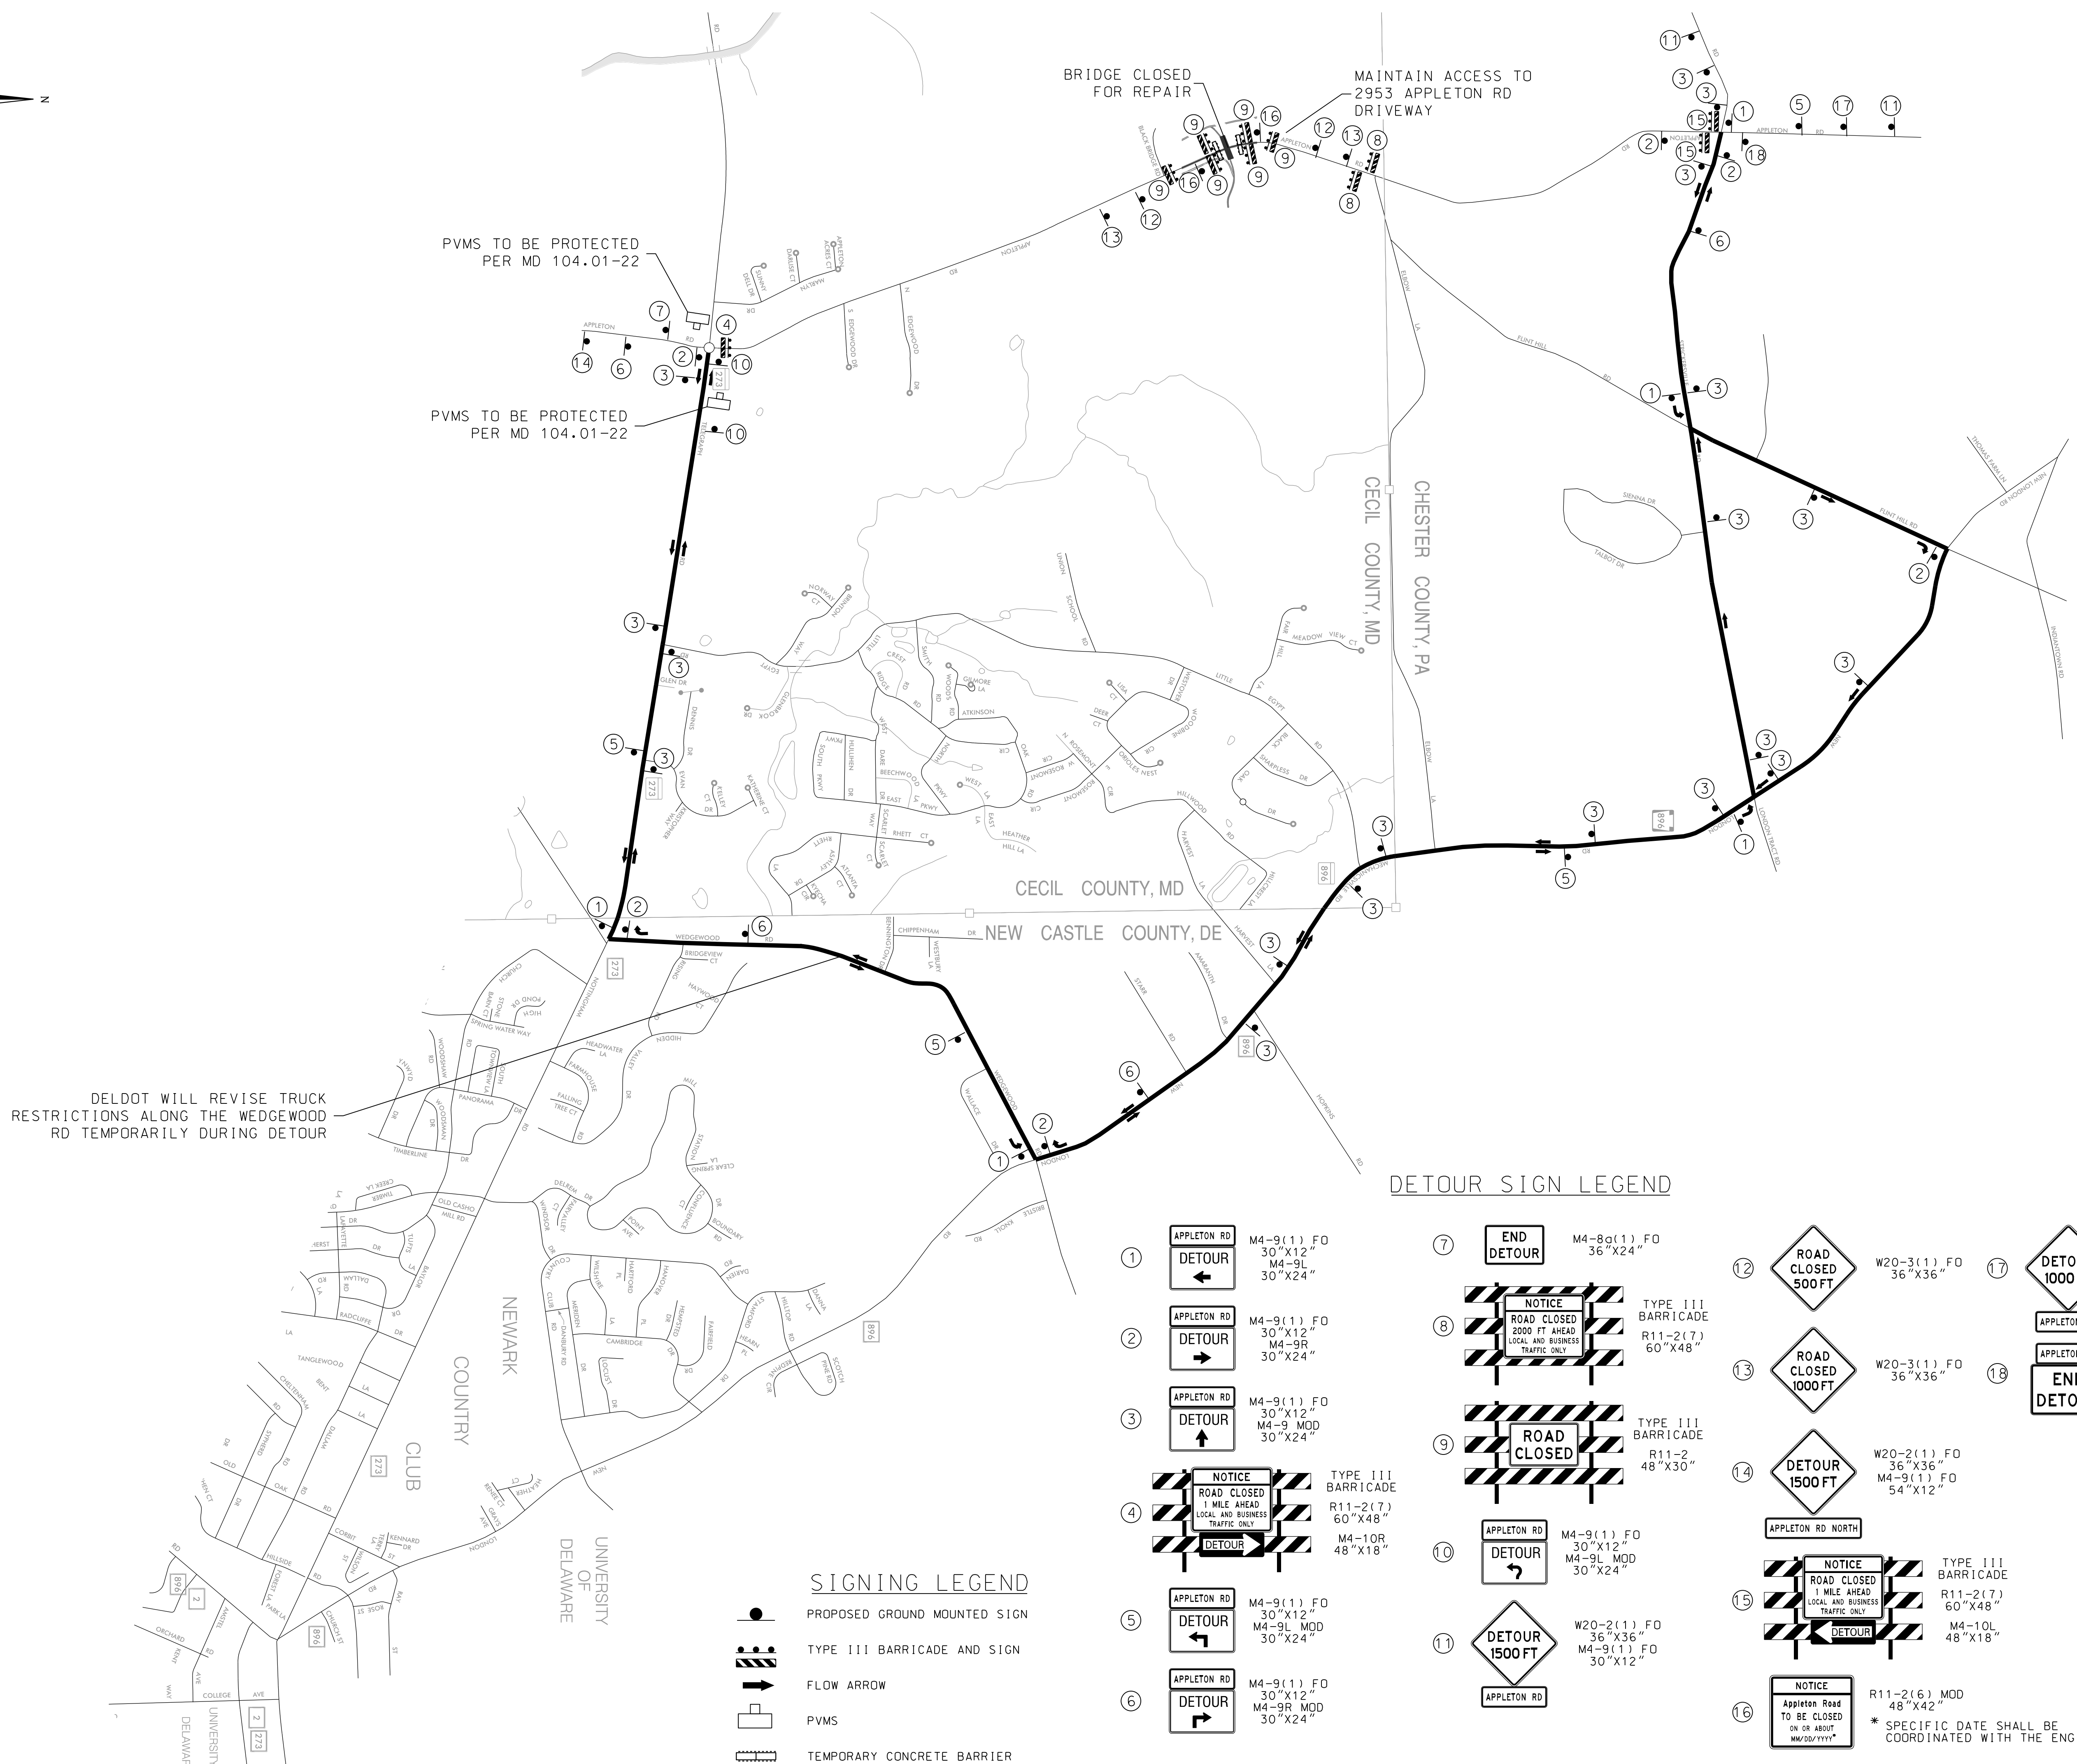

DELDOT WILL REVISE TRUCK RESTRICTIONS ALONG THE WEDGEWOOD RD TEMPORARILY DURING DETOUR

PVMS TO BE PROTECTED PER MD 104.01-22


PVMS TO BE PROTECTED PER MD 104.01-22

SIGNING LEGEND

- PROPOSED GROUND MOUNTED SIGN
- TYPE III BARRICADE AND SIGN
- FLOW ARROW
- PVMS
- TEMPORARY CONCRETE BARRIER

DETOUR SIGN LEGEND

1	APPLETON RD DETOUR ← M4-9(1) FO 30"x12" M4-9R 30"x24"	7	END DETOUR M4-8(1) FO 36"x24"	12	ROAD CLOSED 500 FT W20-3(1) FO 36"x36"	17	DETOUR 1000 FT APPLETON RD M4-9(1) FO 30"x12"
2	APPLETON RD DETOUR → M4-9(1) FO 30"x12" M4-9R 30"x24"	8	NOTICE ROAD CLOSED 2000 FT AHEAD LOCAL AND BUSINESS TRAFFIC ONLY TYPE III BARRICADE R11-2(7) 60"x48"	13	ROAD CLOSED 1000 FT W20-3(1) FO 36"x36"	18	APPLETON RD END DETOUR M4-9(1) FO 30"x12" M4-8(1) FO 36"x24"
3	APPLETON RD DETOUR ↑ M4-9(1) FO 30"x12" M4-9 MOD 30"x24"	9	ROAD CLOSED TYPE III BARRICADE R11-2 48"x30"	14	DETOUR 1500 FT APPLETON RD NORTH W20-2(1) FO 36"x36" M4-9(1) FO 54"x12"		
4	NOTICE ROAD CLOSED 1 MILE AHEAD LOCAL AND BUSINESS TRAFFIC ONLY DETOUR TYPE III BARRICADE R11-2(7) 60"x48" M4-10R 48"x18"	10	APPLETON RD DETOUR ↘ M4-9(1) FO 30"x12" M4-9L MOD 30"x24"	15	NOTICE ROAD CLOSED 1 MILE AHEAD LOCAL AND BUSINESS TRAFFIC ONLY DETOUR TYPE III BARRICADE R11-2(7) 60"x48" M4-10L 48"x18"		
5	APPLETON RD DETOUR ↙ M4-9(1) FO 30"x12" M4-9L MOD 30"x24"	11	DETOUR 1500 FT APPLETON RD W20-2(1) FO 36"x36" M4-9(1) FO 30"x12"	16	NOTICE Appleton Road TO BE CLOSED ON OR ABOUT MM/DD/YYYY R11-2(6) MOD 48"x42" * SPECIFIC DATE SHALL BE COORDINATED WITH THE ENGINEER		
6	APPLETON RD DETOUR ↗ M4-9(1) FO 30"x12" M4-9R MOD 30"x24"						



\\net.rkk.com\In\Cloud\Projects\2018\18021_0051700700\Task_05 - Appleton Rd Bridge Replacement\CAD\Drawings\001 - Appleton.dwg
